


序号	报告编号	发布日期	结论	影像资料
21	GX-B1598/21-5-23022	2023/8/10	实测钢丝绳有效截面积损失百分比最大为2.05%，小于5%为正常。	
22	GX-B1598/21-5-23023	2023/8/10	实测钢丝绳有效截面积损失百分比最大为2.03%，小于5%为正常。	



23	GX-B1598/21-5-23024	2023/8/10	实测钢丝绳有效截面积损失百分比最大为1.26%，小于5%为正常。	 A photograph showing a worker in a red hard hat and blue uniform operating machinery in an industrial setting. The worker is looking at a device or control panel. The background shows various pipes and equipment. A red date stamp '2023年7月16日' is visible in the bottom right corner of the image.
24	GX-B1598/21-5-23025	2023/8/10	实测钢丝绳有效截面积损失百分比最大为1.14%，小于5%为正常。	 A photograph showing a worker in a red hard hat and blue uniform holding a laptop in an industrial setting. The worker is standing near a large piece of machinery. The background shows various pipes and equipment. A red date stamp '2023年7月16日' is visible in the bottom right corner of the image.

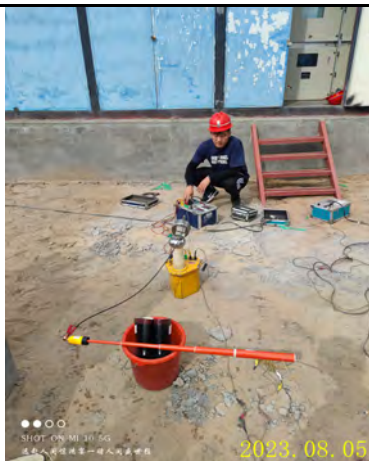
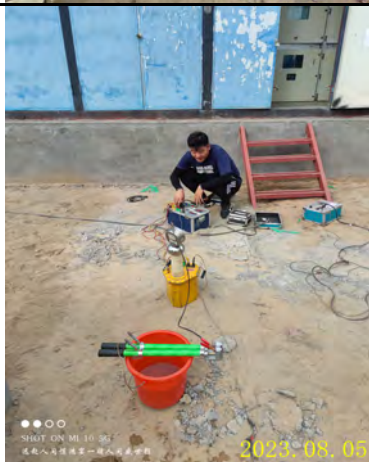
25	GX-B1598/21-5-23036	2023/8/10	实测钢丝绳有效截面积损失百分比最大为2.43%，小于5%为正常。	 <p>2023年7月17日</p>
26	GX-B1598/21-5-23037	2023/8/10	实测钢丝绳有效截面积损失百分比最大为2.31%，小于5%为正常。 。	 <p>2023年7月17日</p>

27	GX-B1598/21-5-23038	2023/8/10	实测钢丝绳有效截面积损失百分比最大为3.41%，小于5%为正常。	
28	GX-B1598/21-5-23039	2023/8/10	实测钢丝绳有效截面积损失百分比最大为2.89%，小于5%为正常。	

29	GX-B1598/21-5-23040	2023/8/10	实测钢丝绳有效截面积损失百分比最大为0.83%，小于5%为正常。	
30	GX-B1321/20-5-23876~23877	2023. 8. 15	本次共检电力电缆2条，2条电力电缆所检项目合格。	

31	GX-B1312/20-5-23509~23511	2023. 8. 15	本次共检电力变压器3台，3台电力变压器所检项目合格。		 A photograph showing a worker in a dark environment, possibly a tunnel or underground facility, wearing a hard hat and safety gear. The worker is focused on inspecting or working on a piece of electrical equipment. A bright light source is visible, illuminating the scene. A yellow timestamp '2023.08.01' is at the bottom right.	
32	GX-B1350/21-5-23062	2023. 8. 15	所检项目合格。		 A photograph of a worker in a blue uniform and black pants standing outdoors on a dirt mound. The worker is looking down at a device in their hands. In the background, there are blue structures and a building. A yellow timestamp '2023.08.05' is at the bottom right.	

33	GX-B1328/20-5-23146	2023. 8. 15	本次共检绝缘手套6只，6只绝缘手套合格。	
34	GX-B1328/20-5-23147	2023. 8. 15	本次共检绝缘鞋6只，6只绝缘鞋合格。	

35	GX-B1328/20-5-23148	2023. 8. 15	所检项目合格。		 <p>SHOT ON MI 10 5G 2023.08.05</p>
36	GX-B1328/20-5-23149	2023. 8. 15	所检项目合格。		 <p>SHOT ON MI 10 5G 2023.08.05</p>



37	GX-B1312/20-5-23512~23514	2023. 8. 15	本次共检电力变压器3台，3台电力变压器所检项目合格。	 <p>A photograph showing a worker in a red hard hat and blue shirt standing next to a large blue electrical transformer. The worker is holding a tool or device. The transformer is mounted on a concrete base. The background shows other industrial equipment and a clear sky. A yellow timestamp '2023.08.15' is visible in the bottom right corner of the photo.</p>
38	GX-B1300/20-5-23021	2023/8/14	所检项目合格。	 <p>A photograph showing a worker in a red hard hat and white shirt standing next to a large green electrical transformer indoors. The worker is holding a tool or device. The transformer is mounted on a concrete base. The background shows other industrial equipment and a clear sky. A yellow timestamp '2023/8/14' is visible in the bottom right corner of the photo.</p>

39	GX-B1598/21-5-23059	2023/8/17	实测钢丝绳有效截面积损失百分比最大为4.96%，小于5%为正常。	
40	GX-B1598/21-5-23060	2023/8/17	实测钢丝绳有效截面积损失百分比最大为2.06%，小于5%为正常。	



41	GX-B1598/21-5-23061	2023/8/17	实测钢丝绳有效截面积损失百分比最大为1.24%，小于5%为正常。	
42	GX-B1598/21-5-23062	2023/8/17	实测钢丝绳有效截面积损失百分比最大为2.03%，小于5%为正常。	

43	GX-B1598/21-5-23049	2023/8/18	实测钢丝绳有效截面积损失百分比最大为2.05%，小于5%为正常。			
44	GX-B1598/21-5-23050	2023/8/18	实测钢丝绳有效截面积损失百分比最大为2.03%，小于5%为正常。			

45	GX-B1598/21-5-23051	2023/8/18	实测钢丝绳有效截面积损失百分比最大为1.26%，小于5%为正常。	
46	GX-B1598/21-5-23052	2023/8/18	实测钢丝绳有效截面积损失百分比最大为1.14%，小于5%为正常。	

47	GX-B1312/20-5-23508	2023/8/17	所检项目合格。	
48	GX-B1321/20-5-23875	2023/8/17	所检项目合格。	


49	GX-B1310/21-5-23214	2023. 8. 17	符合标准要求。	
50	GX-B1306/21-5-23058	2023. 8. 18	所检项目合格	

51	GX-B1306/21-5-23059	2023. 8. 18	所检项目合格	
52	GX-B1306/21-5-23060	2023. 8. 18	所检项目合格	



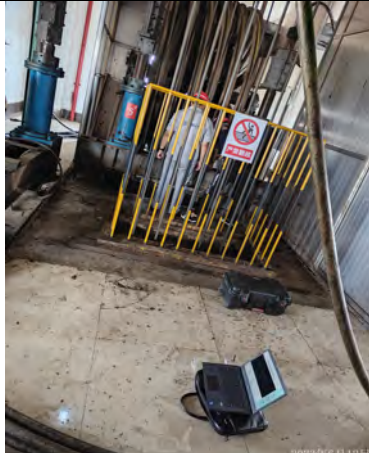
53	GX-B1306/21-5-23061	2023. 8. 18	所检项目合格	
54	GX-B1306/21-5-23062	2023. 8. 18	所检项目合格	

55	GX-B1306/21-5-23063	2023. 8. 18	所检项目合格	
56	GX-B1306/21-5-23064	2023. 8. 18	所检项目合格	

57	GX-B1300/20-5-23023	2023. 8. 18	所检项目合格	
58	GX-B1300/20-5-23022	2023. 8. 21	所检项目合格。	

59	GX-B1310/21-5-23222	2023. 8. 22	符合标准要求。	
60	GX-B1310/21-5-23223	2023. 8. 22	符合标准要求。	

61	GX-B1310/21-5-23224	2023. 8. 22	符合标准要求。			
62	GX-B1310/21-5-23225	2023. 8. 22	符合标准要求。			

63	GX-B1598/21-5-23053	2023/8/23	实测钢丝绳有效截面积损失百分比最大为2.68%，小于5%为正常。	
64	GX-B1598/21-5-23054	2023/8/23	实测钢丝绳有效截面积损失百分比最大为1.76%，小于5%为正常。	

65	GX-B1598/21-5-23055	2023/8/23	实测钢丝绳有效截面积损失百分比最大为3.02%，小于5%为正常。	
66	GX-B1598/21-5-23056	2023/8/23	实测钢丝绳有效截面积损失百分比最大为1.42%，小于5%为正常。	

67	GX-B1598/21-5-23057	2023/8/23	实测钢丝绳有效截面积损失百分比最大为2.00%，小于5%为正常。 。	
68	GX-B1598/21-5-23058	2023/8/23	实测钢丝绳有效截面积损失百分比最大为3.11%，小于5%为正常。	
